

Project Budget Calculator

User guide: every sheet, every column, every formula

Workbook: **Project_Budget_Calculator.xlsx**

Based on: the *Revenue Forecast Calculator* slide and the clarifications agreed on 6 October 2026

Capacity: 50 projects · up to 24 months per project · 36-month calendar timeline (Jan 2026 – Dec 2028 by default)

About the screenshots. The screenshots in this guide use six sample projects so that every view has something to show. Empty project rows are hidden in the screenshots so the totals rows fit. The delivered workbook has only the one example row from the slide. Overwrite it or delete it when you add your own projects.

Contents

1. Overview	3
1.1 The two formulas	3
1.2 How the sheets fit together	3
1.3 Colour conventions	3
2. Getting started	4
2.1 First-time setup	4
2.2 The monthly routine	4
2.3 Adding, filtering and visualising	4
3. Key concepts	5
3.1 Current Month: actuals vs forecast	5
3.2 Phasing weights and renormalisation	5
3.3 Worked example: the slide	5
4. Sheet-by-sheet reference	6
4.1 README	6
4.2 Projects (Project Σ Table)	7
4.3 Phasing	8
4.4 WIP Log	11
4.5 Project Page	12
4.6 Timeline	15
4.7 Aggregator	15
4.8 Phased Budget (calculation grid)	18
5. Status messages and troubleshooting	20
5.1 Other things to check	20
6. More worked examples	22
6.1 Equal weights: Data Platform Migration	22
6.2 Shaped weights after a slow start: Cloud Cost Review	22
6.3 A project that hasn't started: Security Audit	22
6.4 A finished project: CRM Rollout	22
7. Limits and changing the size	23
7.1 Things the workbook does not do	23
7.2 Glossary	23

1. Overview

The workbook keeps a portfolio of projects and answers one question for each of them: **how much of the contracted budget is still to be earned, and in which months?** That remaining amount is the **Budgeted** balance. The workbook spreads it over the months the project has left, using a phasing profile you choose.

1.1 The two formulas

Everything in the workbook comes from two rules on the original slide:

$$\text{Budgeted} = \text{Contracted Budget} - \text{WIP to date}$$

$$\text{Phased Budgeted}(k) = \text{Budgeted} \times \text{weight}(k) \div \sum \text{weights of the remaining months}$$

WIP to date is the sum of the WIP actuals you have logged for every month up to and including the **Current Month**. The **remaining months** are the project months after the Current Month. The weights of those months are renormalised so they add up to 1.0. That way the whole Budgeted balance, no more and no less, lands in the months that are left.

1.2 How the sheets fit together

Sheet	Role	You type here?	Slide page
README	Built-in quick reference	No	–
Projects	Project Σ table: master list, Current Month, key results, status	Yes	1 · Project Σ Table
Phasing	Raw phasing weights per project month	Yes	(Phasing inputs)
WIP Log	Monthly WIP actuals on the calendar	Yes	(WIP inputs)
Project Page	Detail and chart for one selected project	Only the selector	2 · Project Page
Timeline	Gantt-style view of every project, month by month	No	3 · Project Timeline
Aggregator	Portfolio totals per month and per year against TRM	Only TRM	4 · Aggregator
Phased Budget	Calculation grid feeding the views	No	–

Data flows one way: **Projects + Phasing + WIP Log → Phased Budget → Project Page, Timeline and Aggregator**. Every project sits on the same row number on every per-project sheet (project 1 is row 6, project 50 is row 55). So when you look at row 9 on the Phasing sheet, you are looking at the same project as row 9 on Projects.

1.3 Colour conventions

Look	Meaning	Where
Blue text	A value you type (hard-coded input)	Project fields, weights, WIP amounts, TRM
Yellow fill	A key setting or selector	Current Month, Timeline Start, TRM column, project selector
Light-yellow fill	Input cell inside the project's active window	Phasing and WIP Log grids
Grey fill	Calculated column, or a cell outside the project's window	Projects calc columns; Phasing / WIP Log grids

Look	Meaning	Where
Black text	Formula: don't overwrite	All calculated cells
Green text	A link that pulls a value from another sheet	Names, dates and figures repeated across sheets
Red / pink highlight	Something needs your attention	Status column; WIP logged in a future month

2. Getting started

2.1 First-time setup

1. **Set the Timeline Start** (Projects!C3) to the first month you want on the calendar. The default is Jan 2026. Do this *before* logging any WIP (see the warning in section 4.4).
2. **Set the Current Month** (Projects!C2) to the latest month whose WIP you know. The default is Oct 2026.
3. **Delete or overwrite the example row** on Projects (row 6), together with its weights on Phasing row 6 and its 1,000 WIP in Oct 2026 on WIP Log row 6.
4. **Add your projects** on Projects: Name, Engagement Manager, Starting Month, Duration, Contracted Budget. Use the next empty row each time.
5. **Enter phasing weights** on Phasing for each project, or leave the row blank for equal weights.
6. **Log any WIP to date** on WIP Log, in the calendar-month columns.
7. **Check the Status column** on Projects. Every project should read *OK*.

2.2 The monthly routine

Once set up, each month-end comes down to two edits:

1. On **WIP Log**, enter the WIP actual for the month just closed, for each project.
2. On **Projects**, move **Current Month** forward one month.

That is all. WIP to date, Budgeted, the remaining months, the re-phased forecast, the timeline, the project page and the aggregator all recalculate. Any shortfall or overrun in the month you just closed is spread automatically over the months that are left.

Tip: the order matters only for a moment. WIP logged in a month *after* the Current Month is ignored (and shown struck through in red) until the Current Month reaches it. So you can log it first and move the month second, or the other way round.

2.3 Adding, filtering and visualising

The slide asks for *create new*, *filter* and *visualize* buttons. Excel can't add real buttons without macros, so the workbook does this instead:

Slide button	In the workbook
Create new	Type the new project into the next empty row on Projects. All 50 rows are already wired through every sheet, so nothing else needs to be copied.
Filter	Use the filter arrows in the Projects header row. For example, filter on Engagement Manager or Status.
Visualize	Go to Project Page and pick the project in the yellow dropdown, or look at Timeline / Aggregator.

3. Key concepts

3.1 Current Month: actuals vs forecast

The Current Month is the line between the past and the future. For every project:

- Months **up to and including** the Current Month are **actuals**. Their value is the WIP you logged.
- Months **after** the Current Month are **forecast**. Their value is the Phased Budgeted amount.
- Moving the Current Month forward turns a forecast month into an actual month. The Budgeted balance is then re-spread over the smaller set of months that are left.

Only the year and month of the date count, so 1 Oct 2026 and 17 Oct 2026 are treated the same.

3.2 Phasing weights and renormalisation

Weights describe the shape of a project's workload. Enter them as any non-negative numbers, for example 1, 2, 2, 2, 2 or 10%, 20%, 20%, 25%, 25%. Only their relative size matters. The workbook renormalises them twice:

- **Over the full duration**, for the *plan weights* on Phasing (the right-hand block) and the *Original Plan* column on Project Page. They always add up to 100%.
- **Over the remaining months only**, for the Phased Budgeted forecast. The weights of months already in the past drop out, and the rest are scaled back up to 100%.

If a project has **no weights at all**, every month gets weight 1 (equal phasing). If some weights are entered, blank months count as 0.

3.3 Worked example: the slide

The slide shows a five-month project phased I 1k · II 2k · III 2k · IV 2k · V 2k. As agreed: contract **10,000**, weights **1 : 2 : 2 : 2 : 2**, start Oct 2026, and **1,000** of WIP logged in month I (Oct 2026, the Current Month).

Step	Calculation	Result
WIP to date	WIP logged for months $\leq$ Oct 2026	1,000
Budgeted	$10,000 - 1,000$	9,000
Remaining months	Nov 2026 – Feb 2027 (months II–V)	4
Remaining weights	$2 + 2 + 2 + 2$	8
Phased Budgeted per month	$9,000 \times 2 \div 8$	2,250
Check	$1,000 \text{ actual} + 4 \times 2,250 \text{ forecast}$	$10,000 = \text{contract } \checkmark$

Compare the *Original Plan* on Project Page: $10,000 \times 1/9 = 1,111$ for month I and $10,000 \times 2/9 = 2,222$ for each later month. Month I came in 111 below plan, and that 111 is now spread across months II–V (2,250 instead of 2,222).

4. Sheet-by-sheet reference

Each section below covers what the sheet is for, what it looks like, every column, what you type, and how its numbers are worked out. Wide sheets are shown in several screenshots (12 months at a time, names repeated), and the unused project rows (7–50) are hidden so the totals rows fit.

4.1 README

A one-page summary inside the workbook covering the formulas, the sheet list, the colour key, the monthly routine and the limits. It has no formulas and no inputs. Keep it as a quick reminder for colleagues who get the file without this guide.

Project Budget Calculator

PURPOSE	Calculates the Budgeted balance of each project and phases it over the remaining months of the project.
FORMULAS	
Budgeted	Budgeted = Contracted Budget – WIP to date (the sum of WIP logged in months up to and including the Current Month). Budgeted is spread only over the project months AFTER the Current Month, using that project's phasing weights for those months, renormalised to 1.0.
Phased Budgeted	Phased Budgeted (month k) = Budgeted × weight(k) ÷ Σ weights of remaining months. Enter raw weights (e.g. 1,2,2,2,2). They don't need to sum to 1. If a project has no weights at all, every month gets an equal weight.
Weights	
Example (from the slide)	Contract 10,000. 5 months, weights 1:2:2:2:2. 1,000 of WIP logged in month I (the current month). → Budgeted = 9,000, phased over months II–V (weights 2:2:2:2 → 25% each) = 2,250 per month.
SHEETS	
Projects	Project Σ table (page 1). Holds the global Current Month field. Add a project by filling in the next empty row. Use the header filter buttons to filter.
Phasing	Raw phasing weights per project, month 1–24 of the project. Also shows the weights normalised to 1.0 over the full duration.
WIP Log	Monthly WIP actuals per project on the calendar timeline. Only months ≤ Current Month count towards WIP to date.
Project Page	Page 2: pick a project from the dropdown to see its details, month-by-month phasing and chart (the "visualize" view).
Timeline	Page 3: Gantt-style view of every project. Each cell shows the WIP actual (≤ Current Month) or the Phased Budgeted (after it).
Aggregator	Page 4: Σ WIP + Σ Phased Budgeted per month against the manual TRM input, with a chart and calendar-year totals.
Phased Budget	Calculation grid (no inputs): Phased Budgeted per project per calendar month.
HOW TO USE	
Yellow cells	Key inputs: Current Month, Timeline Start, the TRM row and the project selector.
Blue text	Hard-coded inputs: project fields, weights, WIP amounts. Black text = formulas. Green text = links to another sheet.
Light yellow grids	Input grids on Phasing and WIP Log. Grey cells there are outside the project's duration or window.
Monthly routine	1) Log the month's WIP on WIP Log. 2) Move Current Month forward one month on Projects. Everything recalculates.
Status column	Projects!N flags problems: WIP above contract, no remaining months left to phase the budget into, missing fields, etc.
LIMITS & ASSUMPTIONS	
Capacity	50 projects, durations up to 24 months, calendar timeline of 36 months from Timeline Start (default Jan 2026 – Dec 2028).
Timeline Start	Change it only before logging WIP: the WIP Log columns are tied to calendar months, so moving the start shifts those columns.
Months	Starting Month and Current Month are compared by year and month only (the day is ignored).
Units	All amounts are in one currency unit (enter 10000 for 10k). No currency symbol is applied.
TRM	Monthly comparison target, entered manually on the Aggregator sheet (per user).
Annual totals	Calendar years (Jan–Dec), WIP actuals + Phased Budgeted.
Source	Logic from "Revenue_Forecast_Calculator.pptx", with the user's clarifications from 2026-10-06.

Figure 1: README sheet

4.2 Projects (Project Σ Table)

The master list and the main place to work. Each row is one project: you fill in the first five fields and the sheet works out the rest. The two settings at the top drive the whole workbook.

Settings

Cell	Name	What it does
C2	Current Month	Divides actuals ($\leq$) from forecast ($>$). Move it forward one month each month-end.
C3	Timeline Start	First month of the 36-month calendar used by WIP Log, Phased Budget, Timeline and Aggregator. Set it once, before you log WIP.

Columns (rows 6-55, one project per row)

Col	Header	Type	Meaning / formula
A	#	-	Project slot number 1-50.
B	Project Name	Input	Must be unique. It is the key used by the Project Page dropdown. A row with no name is ignored everywhere.
C	Engagement Manager	Input	Free text. Handy for filtering.
D	Starting Month	Input	Any date in the first month of the project. Shown as "Oct 2026".
E	Duration (months)	Input	Whole number 1-24 (enforced by data validation).
F	End Month	Calc	Starting Month + Duration – 1 months.
G	Contracted Budget	Input	Total contract value, in plain units (10,000, not 10k).
H	WIP to Date	Calc	From WIP Log column C: the sum of WIP for months $\leq$ Current Month.
I	Budgeted (Contract – WIP)	Calc	G – H. The balance still to be phased.
J	Remaining Months	Calc	Project months after the Current Month: Duration – first remaining month # + 1 (never below 0).
K	Phased Budgeted – Next Month	Calc	The forecast for the month right after the Current Month.
L	Phased Budgeted – Rest of Current Year	Calc	Sum of the forecast for the months after the Current Month, up to December of that year.
M	Current-Year Forecast (WIP + Phased)	Calc	WIP logged in the current year up to the Current Month, plus column L. Gives the project's full-year outturn.
N	Status	Calc	Health check. Reads OK, or names the first problem it finds (see section 5).

Totals row (57) adds up columns G, H, I, K, L and M. Cell N57 counts the projects whose Status is not OK. The **header filters** (row 5) cover all 50 rows, and panes are frozen so the names stay visible as you scroll.

Do not insert or delete rows or columns on any project sheet. Every sheet relies on project n sitting on row $n + 5$. To remove a project, clear its input cells on Projects, Phasing and WIP Log instead.

4.2 Projects: screenshots

Project Σ Table

Current Month

Oct 2026

Timeline Start

Jan 2026

Months up to and including this month are actuals (WIP). Later months are forecast (Phased Budgeted).

First month of the 36-month calendar timeline. Change it only before logging WIP.

#	Project Name	Engagement Manager	Starting Month	Duration (months)	End Month	Contracted Budget
1	Example Project (slide)	J. Doe	Oct 2026	5	Feb 2027	10,000
2	Data Platform Migration	M. Laurent	Jun 2026	12	May 2027	120,000
3	CRM Rollout	A. Okafor	Jan 2026	9	Sep 2026	45,000
4	Security Audit	S. Novak	Mar 2027	4	Jun 2027	30,000
5	Cloud Cost Review	R. Patel	Aug 2026	6	Jan 2027	18,000
6	Analytics Pilot	L. Chen	Sep 2026	3	Nov 2026	9,000
7						
8						
TOTAL						232,000

Figure 2a: Projects, input columns A–G, with the settings at the top and the totals row.

Project Σ Table

Current Month
Timeline Start

#	Project Name	WIP to Date	Budgeted (Contract – WIP)	Remaining Months	Phased Budgeted – Next Month	Phased Budgeted – Rest of Current Year	Current-Year Forecast (WIP + Phased)	Status
1	Example Project (slide)	1,000	9,000	4	2,250	4,500	5,500 OK	
2	Data Platform Migration	45,000	75,000	7	10,714	21,429	66,429 OK	
3	CRM Rollout	45,000	-	-	-	-	45,000 OK	
4	Security Audit	-	30,000	4	-	-	- OK	
5	Cloud Cost Review	11,000	7,000	3	2,333	4,667	15,667 OK	
6	Analytics Pilot	10,500	(1,500)	1	(1,500)	(1,500)	9,000 WIP exceeds contract	
7								
8								
TOTAL		112,500	119,500		13,798	29,095	141,595 1 project(s) need attention	

Figure 2b: Projects, calculated columns H–N. Analytics Pilot is flagged because its WIP (10,500) is above its contract (9,000).

4.3 Phasing

Holds the phasing profile of each project. The grid on the left (**M1–M24**, columns I–AF) is where you type. **M1 is the Starting Month**, M2 the month after, and so on. These are project months, not calendar months. The cells inside the project's duration turn light yellow, and the cells beyond it turn grey.

Col	Header	Meaning / formula
A–C	#, Project Name, Duration	Pulled from Projects (green).
D	Weights entered	How many weight cells have a number. 0 means equal phasing.
E	Σ weights (full duration)	Sum of weights M1...M(Duration), or the Duration itself when no weights are entered.
F	First remaining month #	The project month right after the Current Month. Example: start Aug, Current Month Oct → 4. It is 1 for projects that haven't started yet.
G	Σ weights (remaining months)	Sum of weights from month F to month Duration. This is the divisor in the Phased Budgeted formula. If it is 0 while money is left, Status warns you.
H	Non-zero weights beyond duration	Counts weights typed past the Duration. They are ignored, and Status mentions it.

Col	Header	Meaning / formula
I-AF	M1 ... M24 (input)	Raw weights. Any non-negative number; blanks count as 0 (unless the whole row is blank).
AH-BE	M1 ... M24 (normalised)	Each weight ÷ column E, so the row adds up to 100% over the full duration. These are the plan weights used for the Original Plan on Project Page.
BF	Check Σ	Should show 100.0% for every active project.

Row 2 holds the numbers 1–24 above each block. The formulas use them as month indexes, so leave them alone.

Typical profiles

Profile	Example weights (6 months)	Use when
Flat	(leave blank)	Work is spread evenly
Ramp-up	1, 2, 3, 3, 3, 3	Slow start, steady delivery
Front-loaded	3, 3, 2, 1, 1, 1	Heavy design or set-up phase
Back-loaded	0, 0, 1, 1, 3, 3	Delivery-heavy or acceptance-driven projects
Bell	1, 2, 3, 3, 2, 1	Typical build project

4.3 Phasing: screenshots

Phasing Weights

month index
Enter raw weights in the yellow cells (month 1 = Starting Month). They are renormalised to 1.0 automatically. Leave a row blank for equal weights.

#	Project Name	Duration	Weights entered	Σ weights (full duration)	First remaining month #	Σ weights (remaining months)	Non-zero weights beyond duration
1	Example Project (slide)	5	5	9	2	8	0
2	Data Platform Migration	12	0	12	6	7	0
3	CRM Rollout	9	9	12	11	0	0
4	Security Audit	4	4	6	1	6	0
5	Cloud Cost Review	6	6	8	4	3	0
6	Analytics Pilot	3	0	3	3	1	0
7			0	0	1	0	0
8			0	0	1	0	0

Figure 3a: Phasing helper columns A–H.

Phasing Weights

1 2 3 4 5 6 7 8 9 10 11 12
Enter raw weights in the yellow cells (month 1 = Starting Month). They are renormalised to 1.0 automatically. Leave a row blank for equal weights.

RAW WEIGHTS (input) →													
#	Project Name	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12
1	Example Project (slide)	1	2	2	2	2							
2	Data Platform Migration												
3	CRM Rollout	1	1	2	2	2	1	1	1	1			
4	Security Audit	1	2	2	1								
5	Cloud Cost Review	2	2	1	1	1	1						
6	Analytics Pilot												
7													
8													

Figure 3b: Raw weights M1–M12 (input).

Phasing Weights

13 14 15 16 17 18 19 20 21 22 23 24
Enter raw weights in the yellow cells (month 1 = Starting Month). They are renormalised to 1.0 automatically. Leave a row blank for equal weights.

#	Project Name	M13	M14	M15	M16	M17	M18	M19	M20	M21	M22	M23	M24
1	Example Project (slide)												
2	Data Platform Migration												
3	CRM Rollout												
4	Security Audit												
5	Cloud Cost Review												
6	Analytics Pilot												
7													
8													

Figure 3c: Raw weights M13–M24 (input).

Phasing Weights

1 2 3 4 5 6 7 8 9 10 11 12
Enter raw weights in the yellow cells (month 1 = Starting Month). They are renormalised to 1.0 automatically. Leave a row blank for equal weights.

NORMALISED WEIGHTS, FULL DURATION ($\Sigma = 1.0$) →													
#	Project Name	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12
1	Example Project (slide)	11.1%	22.2%	22.2%	22.2%	22.2%							
2	Data Platform Migration	8.3%	8.3%	8.3%	8.3%	8.3%	8.3%	8.3%	8.3%	8.3%	8.3%	8.3%	8.3%
3	CRM Rollout	8.3%	8.3%	16.7%	16.7%	16.7%	8.3%	8.3%	8.3%	8.3%			
4	Security Audit	16.7%	33.3%	33.3%	16.7%								
5	Cloud Cost Review	25.0%	25.0%	12.5%	12.5%	12.5%	12.5%						
6	Analytics Pilot	33.3%	33.3%	33.3%									
7													
8													

Figure 3d: Normalised weights M1–M12 (columns AH–AS).

Phasing Weights

13 14 15 16 17 18 19 20 21 22 23 24
Enter raw weights in the yellow cells (month 1 = Starting Month). They are renormalised to 1.0 automatically. Leave a row blank for equal weights.

#	Project Name	M13	M14	M15	M16	M17	M18	M19	M20	M21	M22	M23	M24	Check Σ
1	Example Project (slide)													100.0%
2	Data Platform Migration													100.0%
3	CRM Rollout													100.0%
4	Security Audit													100.0%
5	Cloud Cost Review													100.0%
6	Analytics Pilot													100.0%
7														
8														

Figure 3e: Normalised weights M13–M24 and the Σ check (columns AT–BF).

4.4 WIP Log

Monthly WIP actuals for each project, laid out on the **calendar** (columns D–AM = 36 months from the Timeline Start). Type the WIP earned in each month in that month's column.

Area	Meaning
Row 4	"actual" over months ≤ Current Month, "future" over later months.
Row 5	Calendar month headers (Timeline Start, then +1 month each column).
Column C	WIP to Date: the sum of the row for months ≤ Current Month. Feeds Projects column H.
Light-yellow cells	Inside the project's window and ≤ Current Month. The normal place to type.
Grey cells	Outside the project's window. A value here still counts towards WIP to date if ≤ Current Month. It is allowed (for example, late WIP after the end date) but shown on a grey background.
Red, struck-through	A value in a month after the Current Month. It is ignored until the Current Month reaches it.
Row 57	Totals per month. Feeds the Σ WIP column on the Aggregator.

Warning: Timeline Start. WIP values are stored by column, not by date. If you change the Timeline Start after logging WIP, every value moves to a different month. If you ever need to move the timeline, cut and paste the WIP grid sideways by the same number of months first.

WIP can be negative (for example, a reversal). It lowers WIP to date and raises Budgeted.

4.4 WIP Log: screenshots

WIP Log (monthly actuals)

Enter the WIP actual for each project and month. Only months up to and including the Current Month count; later months are ignored.

#	Project Name	WIP to Date (≤ Current Month)	actual	actual	actual	actual	actual	actual	actual	actual	actual	actual	future	future
			Jan 26	Feb 26	Mar 26	Apr 26	May 26	Jun 26	Jul 26	Aug 26	Sep 26	Oct 26	Nov 26	Dec 26
1	Example Project (slide)	1,000										1,000		
2	Data Platform Migration	45,000						9,000	9,000	9,000	9,000	9,000		
3	CRM Rollout	45,000	5,000	5,000	5,000	5,000	5,000	5,000	5,000	5,000	5,000			
4	Security Audit	-												
5	Cloud Cost Review	11,000								4,000	4,000	3,000		
6	Analytics Pilot	10,500									6,000	4,500		
7		-												
8		-												
TOTAL			112,500	5,000	5,000	5,000	5,000	5,000	14,000	14,000	18,000	24,000	17,500	-

Figure 4a: WIP Log, 2026, with the totals row. Light-yellow cells are the active window up to the Current Month (Oct 2026).

WIP Log (monthly actuals)

Enter the WIP actual for each project and month. Only months up to and including the Current Month count; later months are ignored.

#	Project Name	WIP to Date (≤ Current Month)	future	future	future	future	future	future	future	future	future	future	future	future
			Jan 27	Feb 27	Mar 27	Apr 27	May 27	Jun 27	Jul 27	Aug 27	Sep 27	Oct 27	Nov 27	Dec 27
1	Example Project (slide)	1,000												
2	Data Platform Migration	45,000												
3	CRM Rollout	45,000												
4	Security Audit	-												
5	Cloud Cost Review	11,000												
6	Analytics Pilot	10,500												
7		-												
8		-												
TOTAL			112,500	-	-	-	-	-	-	-	-	-	-	-

Figure 4b: WIP Log, 2027 (all "future" at this Current Month).

WIP Log (monthly actuals)

Enter the WIP actual for each project and month. Only months up to and including the Current Month count; later months are ignored.

#	Project Name	WIP to Date (≤ Current Month)	future	future	future	future	future	future	future	future	future	future	future	future
			Jan 28	Feb 28	Mar 28	Apr 28	May 28	Jun 28	Jul 28	Aug 28	Sep 28	Oct 28	Nov 28	Dec 28
1	Example Project (slide)	1,000												
2	Data Platform Migration	45,000												
3	CRM Rollout	45,000												
4	Security Audit	-												
5	Cloud Cost Review	11,000												
6	Analytics Pilot	10,500												
7		-												
8		-												
TOTAL			112,500	-	-	-	-	-	-	-	-	-	-	-

Figure 4c: WIP Log, 2028.

4.5 Project Page

The single-project view ("visualize"). Pick a project in the yellow dropdown at **B3**. The list is the 50 project names from Projects. Everything else on the page fills in for that project.

Header block (rows 5-13)

Engagement Manager, Starting Month, Duration, End Month, Contracted Budget, WIP to Date, Budgeted, Remaining Months and Status, all pulled from the project's row on Projects.

Monthly table (rows 17-40, one row per project month)

Column	Meaning / formula
Project Month	1 ... Duration. Rows past the duration stay blank.
Calendar Month	Starting Month + (k – 1) months.

Column	Meaning / formula
Raw Weight	Weight from Phasing (1 when the project uses equal weights).
Plan Weight ($\Sigma=1$)	Weight normalised over the full duration.
Original Plan	Contracted Budget $\times$ Plan Weight: what the month was worth before any WIP.
WIP Actual	WIP Log value for that calendar month, if $\leq$ Current Month; otherwise 0.
Phased Budgeted	Value from the Phased Budget grid (non-zero only after the Current Month).
Total (WIP + Phased)	Actual for past months plus forecast for future months.
Actual / Forecast	Label for the row.

Row 41 totals the table, and row 42 checks that **Total = Contracted Budget** ("✓ ties"). A difference means part of the budget couldn't be phased (see Status), or that WIP was logged outside the project's months. Cell K1 holds the selected project's row number for the formulas. Don't edit it.

Chart

Stacked columns show **WIP Actual** (blue) and **Phased Budgeted** (red) per month. A green line shows the **Original Plan**, so you can see at a glance where the forecast now differs from the plan.

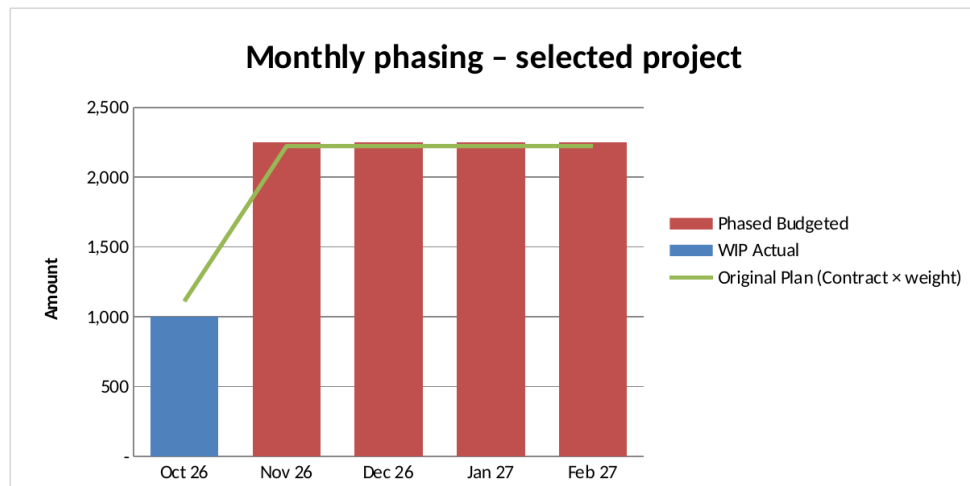


Figure 6: Project Page chart for the slide example: 1,000 actual in Oct, then 2,250 a month against a plan of 2,222.

Project Page

Select project: **Example Project (slide)**

Starting Month	Oct 2026
Duration (months)	5

Duration (months)	5
End Month	Feb 2027

End Month	Feb 2027
Contracted Budget	10.000

Contracted Budget	10,000
WIP to Date	1,000

WIP to Date	1,000
Budgeted (Contract – WIP)	9,000

Budgeted (Contract – WIP)	9,000
Remaining Months	4

Remaining Months	4
Status	OK

Project Month	Calendar Month	Raw Weight	Plan Weight ($\Sigma=1$)	Original Plan (Contract × weight)	WIP Actual	Phased Budgeted	Total (WIP + Phased)	Actual / Forecast
1	Oct 2026	1	11.1%	1,111	1,000	-	1,000	Actual
2	Nov 2026	2	22.2%	2,222	-	2,250	2,250	Forecast
3	Dec 2026	2	22.2%	2,222	-	2,250	2,250	Forecast
4	Jan 2027	2	22.2%	2,222	-	2,250	2,250	Forecast
5	Feb 2027	2	22.2%	2,222	-	2,250	2,250	Forecast
TOTAL			100.0%	10,000	1,000	9,000	10,000	

Figure 5: Project Page for "Example Project (slide)": header block, the 24-row monthly table, the totals row and the "ties" check

4.6 Timeline

A Gantt-style view of the whole portfolio across the 36-month calendar. It is all formulas, with nothing to type. Each cell shows:

- **Dark orange:** the WIP actual for a month $\leq$ Current Month inside the project window.
- **Light orange:** the Phased Budgeted forecast for a month after the Current Month.
- Blank: outside the project window. A WIP value logged outside the window still shows, so it isn't hidden.
- The **red-bordered column** is the Current Month.

Columns A–E show the slot number, name, Engagement Manager, start and end. Use it to spot overlaps, gaps in WIP logging (a white cell inside a project's past months), and months where a lot of forecast bunches up.

Read across a row and the numbers add up to the project's Contracted Budget, as long as its Status is OK.

4.6 Timeline: screenshots

Project Timeline

Dark orange = WIP actual ($\leq$ Current Month). Light orange = Phased Budgeted. The bordered column is the Current Month.

#	Project Name	Engagement Manager	Start	End	Jan 26	Feb 26	Mar 26	Apr 26	May 26	Jun 26	Jul 26	Aug 26	Sep 26	Oct 26	Nov 26	Dec 26
1	Example Project (slide)	J. Doe	Oct 26	Feb 27										1,000	2,250	2,250
2	Data Platform Migration	M. Laurent	Jun 26	May 27						9,000	9,000	9,000	9,000	9,000	10,714	10,714
3	CRM Rollout	A. Okafor	Jan 26	Sep 26	5,000	5,000	5,000	5,000	5,000	5,000	5,000	5,000	5,000			
4	Security Audit	S. Novak	Mar 27	Jun 27												
5	Cloud Cost Review	R. Patel	Aug 26	Jan 27								4,000	4,000	3,000	2,333	2,333
6	Analytics Pilot	L. Chen	Sep 26	Nov 26									6,000	4,500	(1,500)	
7																
8																

Figure 7a: Timeline, 2026. CRM Rollout is complete (all actual). The red-bordered column is the Current Month.

Project Timeline

Dark orange = WIP actual ($\leq$ Current Month). Light orange = Phased Budgeted. The bordered column is the Current Month.

#	Project Name	Engagement Manager	Start	End	Jan 27	Feb 27	Mar 27	Apr 27	May 27	Jun 27	Jul 27	Aug 27	Sep 27	Oct 27	Nov 27	Dec 27
1	Example Project (slide)	J. Doe	Oct 26	Feb 27	2,250	2,250										
2	Data Platform Migration	M. Laurent	Jun 26	May 27	10,714	10,714	10,714	10,714	10,714							
3	CRM Rollout	A. Okafor	Jan 26	Sep 26												
4	Security Audit	S. Novak	Mar 27	Jun 27			5,000	10,000	10,000	5,000						
5	Cloud Cost Review	R. Patel	Aug 26	Jan 27	2,333											
6	Analytics Pilot	L. Chen	Sep 26	Nov 26												
7																
8																

Figure 7b: Timeline, 2027. Security Audit is phased 1:2:2:1 over Mar–Jun 2027.

Project Timeline

Dark orange = WIP actual ($\leq$ Current Month). Light orange = Phased Budgeted. The bordered column is the Current Month.

#	Project Name	Engagement Manager	Start	End	Jan 28	Feb 28	Mar 28	Apr 28	May 28	Jun 28	Jul 28	Aug 28	Sep 28	Oct 28	Nov 28	Dec 28
1	Example Project (slide)	J. Doe	Oct 26	Feb 27												
2	Data Platform Migration	M. Laurent	Jun 26	May 27												
3	CRM Rollout	A. Okafor	Jan 26	Sep 26												
4	Security Audit	S. Novak	Mar 27	Jun 27												
5	Cloud Cost Review	R. Patel	Aug 26	Jan 27												
6	Analytics Pilot	L. Chen	Sep 26	Nov 26												
7																
8																

Figure 7c: Timeline, 2028 (empty for these sample projects, which all end by Jun 2027).

4.7 Aggregator

Portfolio totals. It answers "what is the whole book worth each month and each year, and how does it compare with TRM?"

Monthly table (rows 6-41)

Col	Header	Meaning / formula
A-B	Month, Year	The 36 calendar months and their year.
C	Σ WIP (actual)	WIP Log total for the month, for months $\leq$ Current Month; 0 after.
D	Σ Phased Budgeted	Phased Budget total for the month (non-zero only after the Current Month).
E	Total (WIP + Phased)	C + D: actuals for the past, forecast for the future.
F	TRM (input)	Type your monthly TRM target here (yellow). Leave a month blank if you have no target for it.
G	Variance (Total – TRM)	Positive = ahead of TRM, negative (in brackets) = behind. Blank where TRM is blank.

The Current Month row is shaded. Row 42 totals the columns.

Annual (calendar year) table, I6:N10

For each of the three timeline years: Σ WIP, Σ Phased Budget, **WIP + Phased Budget** (the slide's annual {WIP + Phased Budget}), TRM, and the variance, followed by a total row. Years run January to December.

Reconciliation, I13:M16

Σ Contracted Budget – Σ WIP to date – Σ Phased Budgeted should be **0** ("✓ fully phased"). If it isn't, some budget couldn't be placed in a month: there are no remaining months, the remaining weights are zero, or part of a project falls outside the 36-month timeline. Go to Projects and look at the Status column.

Chart

Stacked columns show **Σ WIP** (blue, the past) and **Σ Phased Budgeted** (red, the future) per month. The **TRM** line (green) sits on top. Past months show WIP because the Phased Budgeted amount is zero by definition once a month becomes actual.

4.7 Aggregator: monthly table

Aggregator

Σ WIP actuals ($\leq$ Current Month) + Σ Phased Budgeted (after it) per month, against TRM. Enter TRM in the yellow column.

Month	Year	Σ WIP (actual)	Σ Phased Budgeted	Total (WIP + Phased)	TRM (input)	Variance (Total – TRM)
Jan 26	2026	5,000	-	5,000	25,000	(20,000)
Feb 26	2026	5,000	-	5,000	25,000	(20,000)
Mar 26	2026	5,000	-	5,000	25,000	(20,000)
Apr 26	2026	5,000	-	5,000	25,000	(20,000)
May 26	2026	5,000	-	5,000	25,000	(20,000)
Jun 26	2026	14,000	-	14,000	25,000	(11,000)
Jul 26	2026	14,000	-	14,000	25,000	(11,000)
Aug 26	2026	18,000	-	18,000	25,000	(7,000)
Sep 26	2026	24,000	-	24,000	25,000	(1,000)
Oct 26	2026	17,500	-	17,500	25,000	(7,500)
Nov 26	2026	-	13,798	13,798	25,000	(11,202)
Dec 26	2026	-	15,298	15,298	25,000	(9,702)
Jan 27	2027	-	15,298	15,298	25,000	(9,702)
Feb 27	2027	-	12,964	12,964	25,000	(12,036)
Mar 27	2027	-	15,714	15,714	25,000	(9,286)
Apr 27	2027	-	20,714	20,714	25,000	(4,286)
May 27	2027	-	20,714	20,714	25,000	(4,286)
Jun 27	2027	-	5,000	5,000	25,000	(20,000)
Jul 27	2027	-	-	-	25,000	(25,000)
Aug 27	2027	-	-	-	25,000	(25,000)
Sep 27	2027	-	-	-	25,000	(25,000)
Oct 27	2027	-	-	-	25,000	(25,000)
Nov 27	2027	-	-	-	25,000	(25,000)
Dec 27	2027	-	-	-	25,000	(25,000)
Jan 28	2028	-	-	-		
Feb 28	2028	-	-	-		
Mar 28	2028	-	-	-		
Apr 28	2028	-	-	-		
May 28	2028	-	-	-		
Jun 28	2028	-	-	-		
Jul 28	2028	-	-	-		
Aug 28	2028	-	-	-		
Sep 28	2028	-	-	-		
Oct 28	2028	-	-	-		
Nov 28	2028	-	-	-		
Dec 28	2028	-	-	-		
TOTAL		112,500	119,500	232,000	600,000	(368,000)

Figure 8: Aggregator monthly table, all 36 months (Jan 2026 – Dec 2028) and the totals row, with a sample TRM of 25,000 a month entered for 2026–2027.

4.7 Aggregator: annual totals and chart

Annual (calendar year)

Year	Σ WIP (actual)	Σ Phased Budget	WIP + Phased Budget	TRM	Variance
2026	112,500	29,095	141,595	300,000	(158,405)
2027	-	90,405	90,405	300,000	(209,595)
2028	-	-	-	-	-
Total	112,500	119,500	232,000	600,000	(368,000)

Reconciliation

Σ Contracted Budget	232,000
Σ WIP to date (all projects)	112,500
Σ Phased Budgeted (on timeline)	119,500
Difference (unphased / off-timeline)	- ✓ fully phased

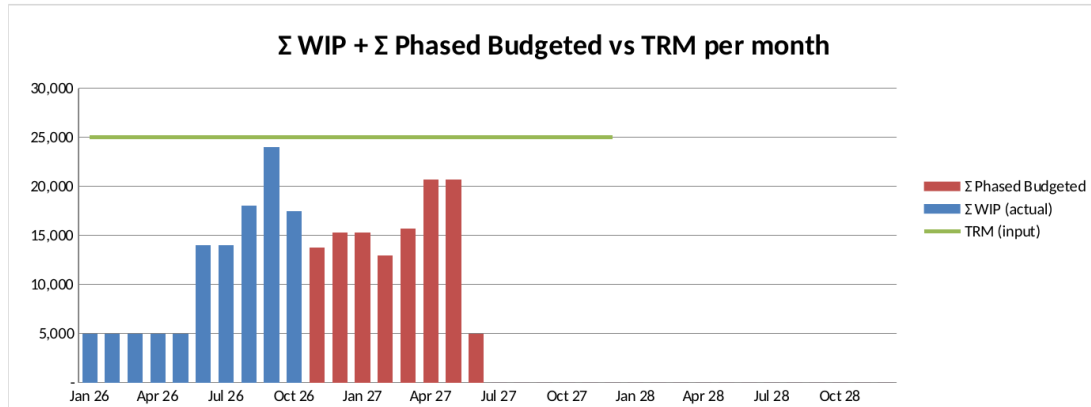


Figure 9: Annual totals, reconciliation (fully phased) and portfolio chart.

4.8 Phased Budget (calculation grid)

The engine room. It has one row per project and one column per calendar month (H-AQ), and each cell holds that project's Phased Budgeted amount for that month. It has no inputs. Every view reads from it.

Col	Header	Meaning
A-D	#, Name, Starting Month, Duration	Pulled from Projects.
E	Budgeted	Projects column I.
F	Σ remaining weights	Phasing column G (the divisor).
G	Equal weights?	TRUE when the project has no weights entered.
H-AQ	Calendar months	The Phased Budgeted amount (formula below).

For calendar month m , the project month is $k = (m - \text{Starting Month}) + 1$. The cell is:

0 if the project is incomplete, Σ remaining weights = 0,
 $m \leq \text{Current Month}$, or k is outside 1 ... Duration
 otherwise Budgeted $\times$ weight(k) $\div$ Σ remaining weights

Row 57 totals each month and feeds the Aggregator.

4.8 Phased Budget: screenshots

Phased Budgeted – calculation grid (no inputs)

$Budgeted \times weight(k) \div \Sigma \text{ remaining weights}$, for project months after the Current Month only.

#	Project Name	Starting Month	Duration	Budgeted	Σ remaining weights	Equal weights?
1	Example Project (slide)	Oct 2026	5	9,000	8	FALSE
2	Data Platform Migration	Jun 2026	12	75,000	7	TRUE
3	CRM Rollout	Jan 2026	9	-	0	FALSE
4	Security Audit	Mar 2027	4	30,000	6	FALSE
5	Cloud Cost Review	Aug 2026	6	7,000	3	FALSE
6	Analytics Pilot	Sep 2026	3	(1,500)	1	TRUE
7				-	0	TRUE
8				-	0	TRUE

TOTAL

119,500

Figure 10a: Phased Budget helper columns A–G.

Phased Budgeted – calculation grid (no inputs)

$Budgeted \times weight(k) \div \Sigma \text{ remaining weights}$, for project months after the Current Month only.

#	Project Name	Jan 26	Feb 26	Mar 26	Apr 26	May 26	Jun 26	Jul 26	Aug 26	Sep 26	Oct 26	Nov 26	Dec 26
1	Example Project (slide)	-	-	-	-	-	-	-	-	-	-	2,250	2,250
2	Data Platform Migration	-	-	-	-	-	-	-	-	-	-	10,714	10,714
3	CRM Rollout	-	-	-	-	-	-	-	-	-	-	-	-
4	Security Audit	-	-	-	-	-	-	-	-	-	-	-	-
5	Cloud Cost Review	-	-	-	-	-	-	-	-	-	-	2,333	2,333
6	Analytics Pilot	-	-	-	-	-	-	-	-	-	-	(1,500)	-
7		-	-	-	-	-	-	-	-	-	-	-	-
8		-	-	-	-	-	-	-	-	-	-	-	-

TOTAL

-

-

-

-

-

-

-

-

-

-

-

13,798

15,298

Figure 10b: Phased Budget, 2026, with the totals row. Values appear only after Oct 2026, the Current Month.

Phased Budgeted – calculation grid (no inputs)

$Budgeted \times weight(k) \div \Sigma \text{ remaining weights}$, for project months after the Current Month only.

#	Project Name	Jan 27	Feb 27	Mar 27	Apr 27	May 27	Jun 27	Jul 27	Aug 27	Sep 27	Oct 27	Nov 27	Dec 27
1	Example Project (slide)	2,250	2,250	-	-	-	-	-	-	-	-	-	-
2	Data Platform Migration	10,714	10,714	10,714	10,714	10,714	-	-	-	-	-	-	-
3	CRM Rollout	-	-	-	-	-	-	-	-	-	-	-	-
4	Security Audit	-	-	5,000	10,000	10,000	5,000	-	-	-	-	-	-
5	Cloud Cost Review	2,333	-	-	-	-	-	-	-	-	-	-	-
6	Analytics Pilot	-	-	-	-	-	-	-	-	-	-	-	-
7		-	-	-	-	-	-	-	-	-	-	-	-
8		-	-	-	-	-	-	-	-	-	-	-	-

TOTAL

15,298

12,964

15,714

20,714

20,714

5,000

-

-

-

-

-

-

-

Figure 10c: Phased Budget, 2027.

Phased Budgeted – calculation grid (no inputs)

$\text{Budgeted} \times \text{weight}(k) \div \sum \text{remaining weights, for project months after the Current Month only.}$

#	Project Name	Jan 28	Feb 28	Mar 28	Apr 28	May 28	Jun 28	Jul 28	Aug 28	Sep 28	Oct 28	Nov 28	Dec 28
1	Example Project (slide)	-	-	-	-	-	-	-	-	-	-	-	-
2	Data Platform Migration	-	-	-	-	-	-	-	-	-	-	-	-
3	CRM Rollout	-	-	-	-	-	-	-	-	-	-	-	-
4	Security Audit	-	-	-	-	-	-	-	-	-	-	-	-
5	Cloud Cost Review	-	-	-	-	-	-	-	-	-	-	-	-
6	Analytics Pilot	-	-	-	-	-	-	-	-	-	-	-	-
7		-	-	-	-	-	-	-	-	-	-	-	-
8		-	-	-	-	-	-	-	-	-	-	-	-
TOTAL		-	-	-	-	-	-	-	-	-	-	-	-

Figure 10d: Phased Budget, 2028.

5. Status messages and troubleshooting

Projects column N checks each project in the order below and shows the **first** problem it finds. Problem rows turn red. N57 counts how many need attention.

Status	Cause	Fix
OK	All checks passed.	–
Missing start / duration / contract	The row has a name but no Starting Month, Duration or Contracted Budget.	Fill in the missing field.
Duration must be 1-24	Duration outside the supported range.	Correct it. For longer projects, see section 7.
WIP exceeds contract	WIP to date > Contracted Budget, so Budgeted is negative and a negative amount is phased.	Check the WIP Log for typos, or raise the contract if it was varied.
Budget not phased: no remaining months	The Current Month is at or past the End Month, but money is still left (or overspent).	Log the missing WIP, extend the Duration, or reduce the contract to what was actually earned.
Budget not phased: remaining weights are 0	Months are left, but every one of their weights is 0.	Put a weight on at least one remaining month on Phasing.
Partly outside timeline	The project starts before Timeline Start or ends after the 36th month. Amounts in those months are not shown.	Expected for old or very long projects. Otherwise check the dates.
Weights entered beyond duration (ignored)	Non-zero weights typed past the project's Duration.	Clear them, or increase the Duration if they were meant to count.

5.1 Other things to check

Symptom	Likely cause
Project Page is blank and shows "Pick a project..."	The name in B3 doesn't match any project name (it was renamed or deleted). Pick it again from the dropdown.
Project Page check shows "X diff"	Budget couldn't be phased (see Status), or WIP was logged outside the project months.
A WIP figure isn't counted	It is in a month after the Current Month (red strike-through). Move the Current Month forward.
Numbers jumped after changing Timeline Start	WIP is stored by column. See the warning in section 4.4.
Two projects get mixed up on Project Page	Duplicate names. The dropdown always finds the first match, so keep names unique.

Symptom	Likely cause
Aggregator reconciliation not 0	At least one project isn't OK. Filter Status on Projects.

6. More worked examples

These use the sample projects in the screenshots, all with the Current Month at Oct 2026.

6.1 Equal weights: Data Platform Migration

Item	Value
Contract / start / duration	120,000 · Jun 2026 · 12 months (Jun 2026 – May 2027) · no weights
WIP logged	$9,000 \times 5 \text{ months (Jun-Oct)} = 45,000$
Budgeted	$120,000 - 45,000 = 75,000$
Remaining months	Nov 2026 – May 2027 = 7 (all weight 1)
Phased Budgeted	$75,000 \div 7 = 10,714 \text{ per month}$

6.2 Shaped weights after a slow start: Cloud Cost Review

Item	Value
Contract / start / duration	18,000 · Aug 2026 · 6 months · weights 2, 2, 1, 1, 1, 1
Original plan	$18,000 \times 2/8 = 4,500$ for Aug and Sep; 2,250 for each later month
WIP logged	Aug 4,000 · Sep 4,000 · Oct 3,000 = 11,000
Budgeted	$18,000 - 11,000 = 7,000$
Remaining months	Nov, Dec, Jan = project months 4–6, weights 1 + 1 + 1 = 3
Phased Budgeted	$7,000 \times 1/3 = 2,333$ per month (each above the 2,250 plan, because Aug–Oct came in 750 under plan)

6.3 A project that hasn't started: Security Audit

Item	Value
Contract / start / duration	30,000 · Mar 2027 · 4 months · weights 1, 2, 2, 1
WIP / Budgeted	0 / 30,000
Phased Budgeted	All four months remain: $30,000 \times 1/6, 2/6, 2/6, 1/6 = 5,000 \cdot 10,000 \cdot 10,000 \cdot 5,000$

6.4 A finished project: CRM Rollout

9 months, Jan–Sep 2026, contract 45,000, with 5,000 of WIP logged every month. WIP to date = 45,000, so Budgeted = 0 and there are no remaining months. Nothing is left to phase, so the Status is *OK*. If the WIP had added up to 44,000, the Status would read *Budget not phased: no remaining months*, flagging the 1,000 that was never earned.

7. Limits and changing the size

Limit	Value	Notes
Projects	50	Rows 6–55 on every project sheet.
Duration per project	24 months	Enforced on Projects column E.
Calendar timeline	36 months	From Timeline Start (default Jan 2026 – Dec 2028).
Annual table	3 calendar years	Follows the timeline.
Units	Plain numbers	No currency symbol. Enter full amounts (10000 for 10k).

The workbook is generated by **tools/build_budget_calculator.py** in the repository. To change the capacity, edit the constants at the top of the script (N = projects, MAXDUR = maximum duration, TL = timeline months), run it, and copy your data across. Don't try to stretch the grids by hand: the row and column layout is the same on every sheet, and hand edits break that.

```
python3 tools/build_budget_calculator.py Project_Budget_Calculator.xlsx
```

7.1 Things the workbook does not do

- There are no macros, so there are no real buttons (see section 2.3).
- It keeps no history of earlier forecasts. Save a copy of the file each month-end if you need snapshots.
- There are no currencies or FX. Every amount is assumed to be in the same unit.
- TRM is typed in by hand each month. It isn't derived from the projects.

7.2 Glossary

Term	Meaning
Contracted Budget	Total agreed value of the project.
WIP	Work in progress: value earned in a month (an actual).
WIP to date	Sum of WIP for months up to and including the Current Month.
Budgeted	Contracted Budget – WIP to date: what is left to earn.
Phasing / weights	The relative share of the work in each project month.
Phased Budgeted	The Budgeted balance spread over the remaining months by their weights.
Remaining months	Project months after the Current Month.
Original Plan	Contract × full-duration weights: the forecast before any WIP.
TRM	The monthly target figure you enter on the Aggregator for comparison.
